

# Final Report

## Carlson Hall Renovation

Project Start: 12/5/2011  
Project End: 10/31/2012  
Lead Contractor Company: J.P. Cullen & Sons, Inc.

Project Type: Alteration/Addition  
Building Type: Academic  
Construction Type: Concrete Frame

Project Recycling Goal: 75.0%

Actual: 83.57%

\*\*\*\*\* Project Totals \*\*\*\*\*

Material Name	Weight (tons)	Volume (yd3)
Diverted Materials		
Cardboard	4.46	89.20
Concrete/Masonry	1,760.04	2516.86
Drywall	36.49	145.96
Metal	87.89	175.78
Other	0.35	0.00
Wood	11.12	74.06
<b>Total Diverted &gt;&gt;&gt;</b>	<b>1,900.35</b>	<b>3,001.86</b>
Solid Waste		
Solid Waste	373.69	2,133.77
<b>Total Solid Waste &gt;&gt;&gt;</b>	<b>373.69</b>	<b>2,133.77</b>
<b>Total for All Materials &gt;&gt;&gt;</b>	<b>2,274.04</b>	<b>5,135.63</b>
<b>Diversion Rate &gt;&gt;&gt;</b>	<b>83.57%</b>	<b>58.45%</b>

# Final Report

## Carlson Hall Renovation

Project Start: 12/5/2011

Project Type: **Alteration/Addition**

Project End: 10/31/2012


Building Type: **Academic**

Lead Contractor Company: **J.P. Cullen & Sons, Inc.**

Construction Type: **Concrete Frame**

Project Recycling Goal: **75.0%**

Actual: **83.57%**

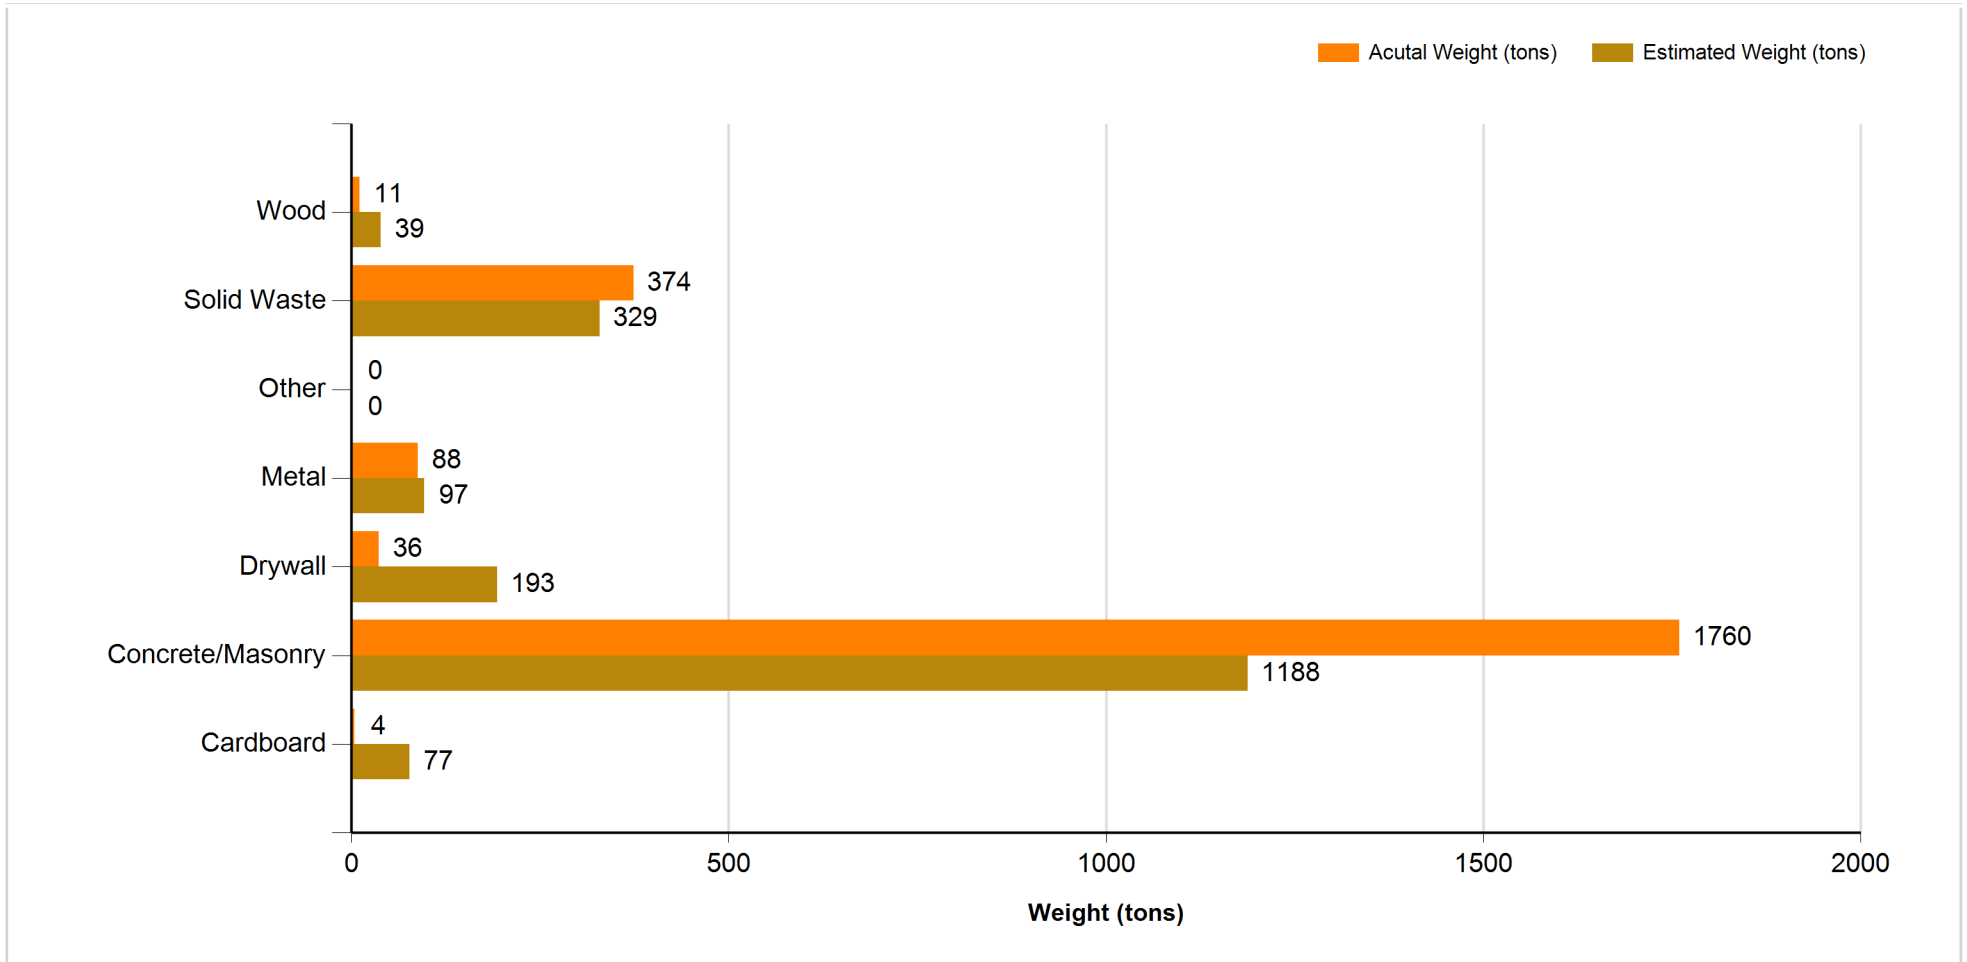

# Final Report

## Carlson Hall Renovation

Project Start: **12/5/2011**

Project Type: **Alteration/Addition**

Project End: **10/31/2012**

Building Type: **Academic**

Lead Contractor Company: **J.P. Cullen & Sons, Inc.**

Construction Type: **Concrete Frame**

Project Recycling Goal: **75.0%**

Actual: **83.57%**

\*\*\*\*\* **Project Totals** \*\*\*\*\*

Material	Hauler/City, State	Destination/City, State	Weight (tons)	Volume (yd3)
Cardboard	Violia Environment Services-Fort Atkinson, WI	A1 Fort Atkinson Veolia-Fort Atkinson, WI	4.46	89.20
Concrete/Masonry	Churchill Trucking-Janesville, WI	Boss Enterprises Inc.-Delavan, WI	1,692.09	2,419.69
Concrete/Masonry	Violia Environment Services-Fort Atkinson, WI	Hausz Bros., Inc.-Ft. Atkinson, WI	67.95	97.17
Drywall	Violia Environment Services-Fort Atkinson, WI	Gypsum Recycling, Inc.-Brooklyn, WI	36.49	145.96
Metal	Alter Metal Recycling-Green Bay, WI	Alter Metal Recycling-Green Bay, WI	21.27	42.54
Metal	Bower's Demo-Black Creek, WI	Kienbaum Iron & Metal-Whitewater, WI	7.13	14.26
Metal	J.P. Cullen & Sons, Inc.-Brookfield, WI	Miller Compressing Co.-Waukesha, WI	1.00	2.00
Metal	J.P. Cullen & Sons, Inc.-Brookfield, WI	Waukesha Iron & Metal, Inc.-Waukesha, WI	1.44	2.88
Metal	Napuck Salvage & Supply, Inc.-Neenah, WI	Napuck Salvage & Supply-Neenah, WI	3.34	6.68
Metal	Sadoff Iron & Metal Co.-Fond du Lac, WI	Sadoff Iron & Metal Co.-Fond du Lac, WI	26.87	53.74
Metal	Violia Environment Services-Fort Atkinson, WI	A1 Fort Atkinson Veolia-Fort Atkinson, WI	11.99	23.98
Metal	Violia Environment Services-Fort Atkinson, WI	Lorman Iron & Metal-Watertown, WI	14.85	29.70
Other	Sadoff Iron & Metal Co.-Fond du Lac, WI	Sadoff Iron & Metal Co.-Fond du Lac, WI	0.35	0.00
Wood	Violia Environment Services-Fort Atkinson, WI	Mallard Ridge-Delavan, WI	11.12	74.06
<b>Total Diverted &gt;&gt;&gt;</b>			<b>1,900.35</b>	<b>3,001.86</b>
Solid Waste	Violia Environment Services-Fort Atkinson, WI	Deer Track Park-Watertown, WI	9.68	55.27
Solid Waste	Violia Environment Services-Fort Atkinson, WI	Janesville City Compost-Janesville, WI	6.82	38.94
Solid Waste	Violia Environment Services-Fort Atkinson, WI	Mallard Ridge-Delavan, WI	357.19	2,039.55

# Final Report

## Carlson Hall Renovation

Project Start: **12/5/2011**

Project Type: **Alteration/Addition**

Project End: **10/31/2012**

Building Type: **Academic**

Lead Contractor Company: **J.P. Cullen & Sons, Inc.**

Construction Type: **Concrete Frame**

---

Project Recycling Goal: **75.0%**

Actual: **83.57%**

---

---

**Total Solid Waste > > >**

**373.69**

**2,133.77**

---

**Total Materials > > >**

**2,274.04**

**5,135.63**

---

**Diversion Rate > > >**

**83.57%**

**58.45%**

---
